





FACILITIES MASTER PLAN PHASE II IMPLEMENTATION
Monthly Report – June 2025



PROJECT ADVOCATES
Your Project. Our Passion.

Westside Community Schools Facilities Master Plan Bond Phase II

Status of Projects by Phase – June 2025

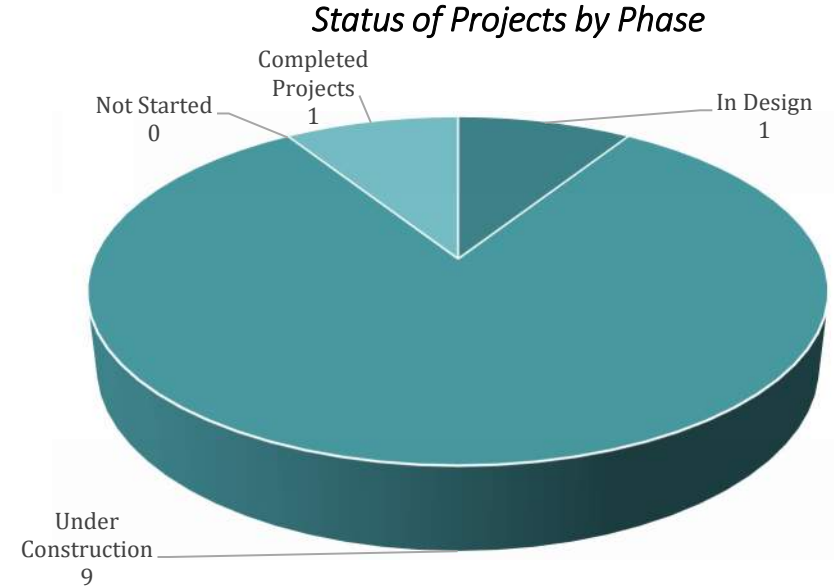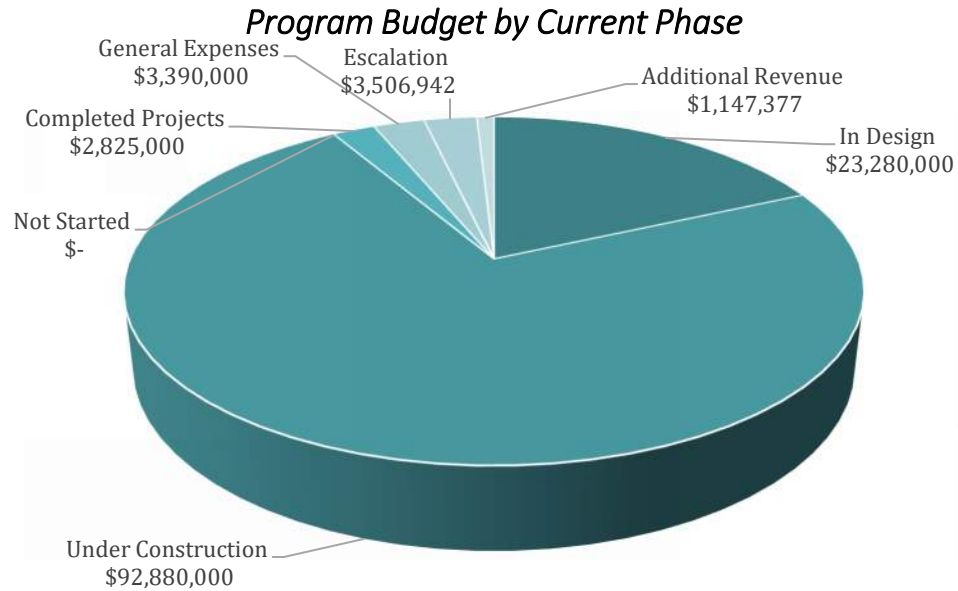


Project Phase	# of Projects	Overall Budget**	Committed Budget	% Committed
In Design	1	\$23,280,000	\$1,476,460	6.3%
Under Construction	9	\$92,880,000	\$82,731,827	89.1%
Not Started	0	\$0	\$0	0.0%
Completed Projects	1	\$2,825,000	\$2,825,000	100.0%
General Expenses	0	\$3,390,000	\$3,347,701	98.8%
Escalation	0	\$3,506,942	\$0	0.0%
Additional Revenue	0	\$1,147,377	\$1,147,377	100.0%
TOTAL	11	\$127,029,319	\$91,528,365	72.1%

*Total number of projects increased from 10 to 11 with the addition of the Security Project.
 **Overall budget will increase each month with the accrual of Bond Interest.


Westside Community Schools Facilities Master Plan Bond Phase II

Status of Overall Program Budget – June 2025

Overall Budget

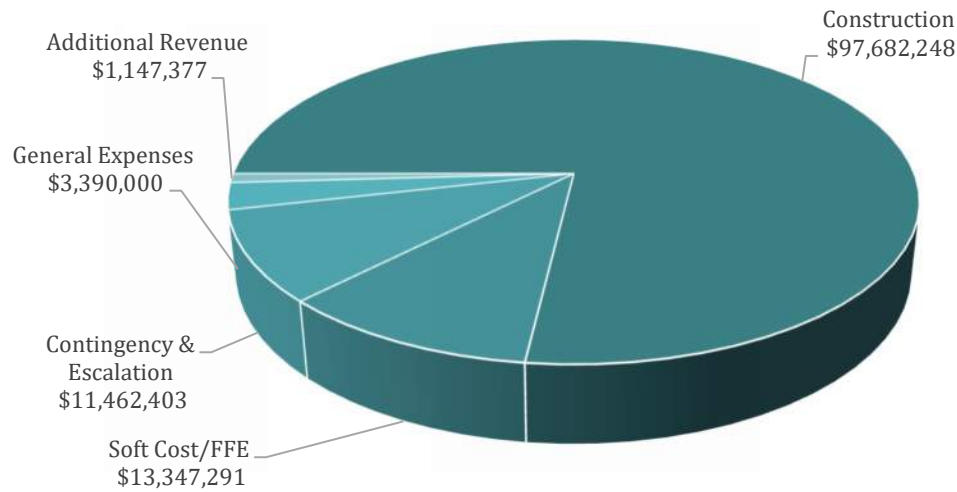

Committed Cost

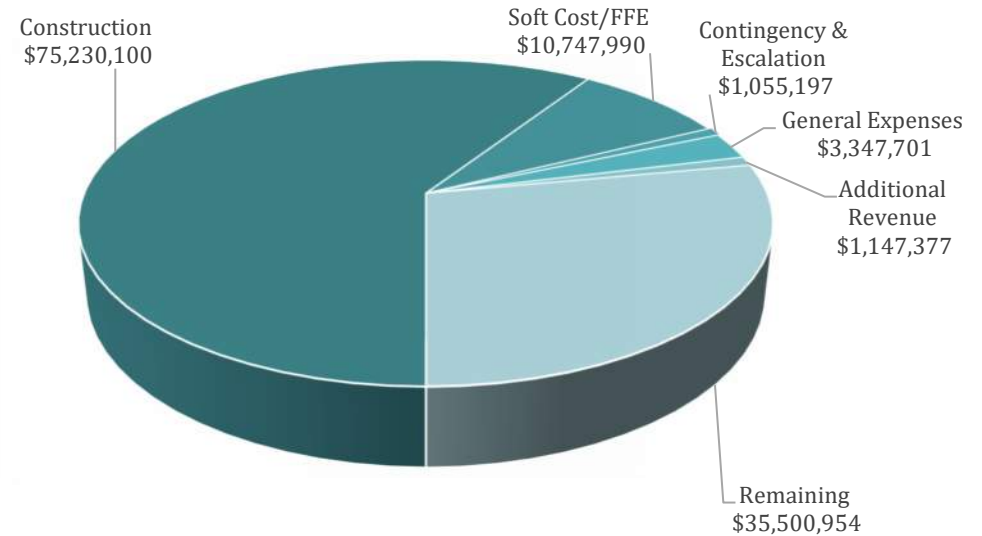

Overall Program Budget Categories	Overall Budget	Committed Cost	% Committed
Construction	\$97,682,248	\$75,230,100	77.0%
Soft Cost/FFE	\$13,347,291	\$10,747,990	80.5%
Contingency & Escalation	\$11,462,403	\$1,055,197	9.2%
General Expenses	\$3,390,000	\$3,347,701	98.8%
Additional Revenue	\$1,147,377	\$1,147,377	100.0%
TOTAL	\$127,029,319	\$91,528,365	72.1%

OVERALL BOND PROGRAM

Summary:

The BOE commissioned an assessment of district facilities in May 2013. This assessment was completed and presented to the BOE in May 2014. The District created a community Task Force to prioritize the projects for Phase II of the Master Plan in 2022. In May 2023, the Westside Community approved a \$121.0 million bond issue with a 63% majority vote. Project Advocates was hired by the District to provide program management services for the implementation of Phase II of the Facilities Master Plan. The value of the work associated with Phase II is \$121.0 million, with the work being completed from FY 2023 through FY 2028. The funds from Phase II will be used to complete new elementary schools at Hillside, Westgate, and Loveland. The funds will also be used for an expanded eating area and infrastructure needs at the middle school and high school; master planning, new gym/storm shelter for Rockbrook and Paddock Road elementary schools; new mechanical and building envelope at Westbrook elementary school; ADA and mechanical updates at the district office; and infrastructure improvements at Underwood Hills.

OVERALL BOND	BUDGET	PROJECTED COST	COMMITTED COST	PAID TO DATE
ABC Building	\$2,825,000	\$2,825,000	\$2,825,000	\$2,798,427
WHS	\$13,580,000	\$13,580,000	\$4,541,103	\$3,790,794
Hillside	\$26,190,000	\$26,190,000	\$25,795,828	\$21,559,520
Loveland	\$23,280,000	\$23,280,000	\$1,476,460	\$171,537
WMS	\$5,200,000	\$5,200,000	\$5,200,000	\$4,937,229
Paddock Road	\$4,795,000	\$4,795,000	\$4,651,035	\$836,459
Rockbrook	\$5,645,000	\$5,645,000	\$5,539,288	\$488,006
Underwood Hills	\$1,395,000	\$1,395,000	\$1,378,185	\$267,015
Westbrook	\$12,515,000	\$12,515,000	\$12,409,450	\$1,568,008
Westgate	\$22,810,000	\$22,810,000	\$22,502,840	\$16,905,355
Security Project	\$750,000	\$750,000	\$714,098	\$614,334
General Expenses	\$3,390,000	\$3,390,000	\$3,347,701	\$1,672,605
Escalation	\$3,506,942	\$3,506,942	\$0	\$0
Additional Revenue	\$1,147,377	\$1,147,377	\$1,147,377	\$1,147,377
Total	\$127,029,319	\$127,029,319	\$91,528,365	\$56,756,666

Community Comments

- Community meeting held at Loveland on June 24, 2025 at 6:00 PM.

Project Updates

- Finishes and site work are in progress at Hillside.
- Finishes and sitework are in progress at Westgate.
- Flooring is in progress at WMS.
- WHS Bathroom work continued.
- Foundations were placed at Paddock Road.
- Demolition and site prep in progress at Rockbrook.
- Mechanical rough in in progress at Westbrook.
- The Loveland concept design was approved by the BOE on June 16, 2025.

HILLSIDE ELEMENTARY



Summary:

Based upon a facilities task force that was completed in December of 2022, Hillside Elementary will be replaced by a new three-section school located on the same site as the current Hillside Elementary School (7500 Western Avenue, Omaha NE, 68114). The current Hillside Elementary School will be decommissioned and razed after the completion of the new school.

This new school will be approximately 64,700 sf and incorporate historical attributes and/or materials from the existing elementary school. It will include: a separate cafeteria and gymnasium, dedicated elective classroom space, improved drop off and pick up access, upgraded security and entrance vestibules, improved ADA access, and the construction of FEMA-rated storm shelters. The new elementary school will need to be designed to allow project-based learning areas. It must also provide a safe, healthy, and secure environment for educators, learners, and staff.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> • Paint is ongoing. • Tile work is in progress. • Ceiling installation is in progress. • Classroom carpet is complete. • MEP finishes are in progress. • The month of July will focus on paint, carpet, tile, exterior sitework, and MEP finishes. 	<ul style="list-style-type: none"> • No new community comments.
	<i>Project Milestones</i>
	<ul style="list-style-type: none"> • Design completion – April 2024/June 2024 • Start construction – May 2024 • Complete new school – September 2025 • Move into new school – October 2025 • Raze old school – June 2026

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$21,521,650	\$22,925,402	\$22,725,402
Soft Cost/FFE	\$3,257,165	\$2,875,003	\$2,680,831
Contingency	\$1,411,185	\$389,595	\$389,595
PROJECT TOTAL	\$26,190,000	\$26,190,000	\$25,795,828

GENERAL INFORMATION

Architect: APMA
 Construction Manager: Boyd Jones
 Project Phase: Under Construction

WESTGATE ELEMENTARY



Summary:

Based upon a facilities task force that was completed in December of 2022, Westgate Elementary will be replaced by a new two-section school located on the same site as the current Westgate Elementary School (7802 Hascall Street, Omaha NE, 68124). The current Westgate Elementary School will be decommissioned and razed after the completion of the new school.

This new school will be approximately 54,500 sf and incorporate historical attributes and/or materials from the existing elementary school. It will include: a separate cafeteria and gymnasium, dedicated elective classroom space, improved drop off and pick up access, upgraded security and entrance vestibules, improved ADA access, and the construction of FEMA-rated storm shelters. The new elementary school will need to be designed to allow project-based learning areas. It must also provide a safe, healthy, and secure environment for educators, learners, and staff.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> • Paint is ongoing. • Tile work is in progress. • Ceiling installation is in progress. • Classroom carpet is complete. • MEP finishes are in progress. • The month of July will focus on paint, carpet, tile, exterior sitework, and MEP finishes. 	<ul style="list-style-type: none"> • No new community comments.
	<i>Project Milestones</i>
	<ul style="list-style-type: none"> • Design completion – April 2024 • Start construction – May 2024 • Complete new school – December 2025 • Move into new school – January 2026 • Raze old school – June 2026

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$18,217,374	\$20,093,842	\$19,883,842
Soft Cost/FFE	\$2,541,738	\$2,559,694	\$2,462,534
Contingency	\$2,050,888	\$156,464	\$156,464
PROJECT TOTAL	\$22,810,000	\$22,810,000	\$22,502,840

GENERAL INFORMATION

Architect: TACK Architects
 Construction Manager: Vrana
 Project Phase: Under Construction

WESTSIDE MIDDLE SCHOOL



Summary:

Based upon a facilities task force that was completed in December of 2022, Westside Middle School will be renovated to expand the cafeteria and upgrade the mechanical systems in those spaces.

Students will remain in the facility during the addition and renovation.

The expansion will expand the seating capacity from 250 to ~375 students and will enhance natural light and views into the space. Existing energy systems and utilities will be modified as required for the cafeteria expansion.

<i>Project Updates</i>		<i>Community Comments</i>	
<ul style="list-style-type: none"> • Ceiling installation is complete. • The cafeteria air handler is operational. Mechanical commissioning has started. • Exterior site cleanup is complete. • Flooring has started. • The month of July will focus on site landscaping and flooring. 		<ul style="list-style-type: none"> • No new community comments. 	
		<i>Project Milestones</i>	
		<ul style="list-style-type: none"> • Design completion – April 2024 • Start construction – May 2024 • Complete addition and renovation – July 2025 	
BUDGET		PROJECTED COST	COMMITTED COST
Construction	\$4,350,000	\$4,528,148	\$4,528,148
Soft Cost/FFE	\$550,000	\$654,414	\$654,414
Contingency	\$300,000	\$17,438	\$17,438
PROJECT TOTAL	\$5,200,000	\$5,200,000	\$5,200,000

GENERAL INFORMATION

Architect: BVH

Construction Manager: Hausmann

Project Phase: Under Construction

WESTSIDE HIGH SCHOOL



Summary:

Based upon a facilities task force that was completed in December of 2022, the Westside High School Building will be renovated to expand the cafeteria and upgrade plumbing systems. The expansion will expand the seating capacity to 550 students and will improve serving area flow. The new space will provide diversity in seating choices. Bathroom remodels will include new waste and vent piping and new bathroom configuration.

Students will remain in the facility during the addition and renovation. Renovations are being planned over the summer months. The bond work will be split into two projects to align with the high school foundation project. One project will be the bathroom renovations and this work is scheduled to occur during the summers of 2024 and 2025. The second project will include the locker room renovations and cafeteria expansion. This project is scheduled to start in the summer of 2026.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> • Restroom set B finishes have started. • The underground and plumbing rough-in of restrooms H and K is complete. • The month of July will focus on finishes for restrooms B and wall framing and finishes for restrooms H and K. • Design for the fluid cooler has begun. 	<ul style="list-style-type: none"> • No new community comments.
	<i>Project Milestones</i>
	<ul style="list-style-type: none"> • Restroom project completion – August 2025 • Cafeteria and Locker-room renovation start – November 2025

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$11,074,350	\$11,578,583	\$3,544,963
Soft Cost/FFE	\$1,745,650	\$1,665,684	\$996,140
Contingency	\$760,000	\$335,733	\$0
PROJECT TOTAL	\$13,580,000	\$13,580,000	\$4,541,103

GENERAL INFORMATION

Architect: BVH
 General Contractor*: 7er Construction/Weitz
 Project Phase: Under Construction

*7er is the General Contractor for the Restroom portion of the project. Weitz is the CMR for the Locker rooms and Cafeteria remodel.

WESTBROOK ELEMENTARY SCHOOL



Summary:

Based upon a facilities task force that was completed in December of 2022, the Westbrook Elementary School will be renovated. The renovations will include new window system and HVAC upgrades.

The Westbrook chiller will need to be replaced prior to the rest of the bond work as it is no longer fully functioning.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> Demo work is complete. Roof curbs have all been set. New roof on the annex building has begun. Soffit framing is complete. Ductwork installation is in progress. The exterior canopy foundations and structural framing is complete. The month of July will focus on ductwork, roofing, ceiling finishes, cleaning, and summer work completion. 	<ul style="list-style-type: none"> No new community comments.
	<i>Project Milestones</i>
	<ul style="list-style-type: none"> Design completion – March 2025 Start construction – June 2025 Complete construction – July 2028

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$10,830,000	\$11,401,672	\$11,362,175
Soft Cost/FFE	\$930,000	\$950,778	\$850,096
Contingency	\$755,000	\$162,550	\$197,179
PROJECT TOTAL	\$12,515,000	\$12,515,000	\$12,409,450

GENERAL INFORMATION

Architect: BCDM
 Construction Manager: Boyd Jones
 Project Phase: Under Construction

PADDOCK ROAD ELEMENTARY SCHOOL



Summary:

Based upon a facilities task force that was completed in December 2022, the Paddock Road Elementary School will have an addition to the facility. The addition will include a gymnasium, two early child classrooms, and a storm shelter. A Campus Master plan will be developed in Phase II for the future Phase III improvements. The future Phase III improvements will utilize the addition being completed in Phase II.

<i>Project Updates</i>	<i>Community Comments</i>	
<ul style="list-style-type: none"> • Site demo is complete. • Sanitary sewer tie-in is complete. • Water main and tie-in is complete. • Storm water systems are in progress. • Foundations are complete. • The month of July will focus on underground building plumbing, site electrical, and precast fabrication and erection. 	<ul style="list-style-type: none"> • No new community comments. 	
	<th><i>Project Milestones</i></th>	<i>Project Milestones</i>
	<ul style="list-style-type: none"> • Design completion – January 2025 • Start construction – May 2025 • Complete addition – June 2026 	

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$4,000,000	\$4,269,478	\$4,194,478
Soft Cost/FFE	\$540,000	\$430,842	\$360,067
Contingency	\$255,000	\$94,680	\$96,490
PROJECT TOTAL	\$4,795,000	\$4,795,000	\$4,651,035

GENERAL INFORMATION

Architect: Leo A. Daly
 Construction Manager: Meco-Henne
 Project Phase: Under Construction

ROCKBROOK ELEMENTARY SCHOOL



Summary:

Based upon a facilities task force that was completed in December 2022, the Rockbrook Elementary School will have an addition to the facility. The addition will include a gymnasium, two early child classrooms, and a storm shelter. A Campus Master plan will be developed in Phase II for the future Phase III improvements. The future Phase III improvements will utilize the addition being completed in Phase II.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> • Site demo is complete. • Over excavation and re-compaction of the soil is in progress. • North playground installation is complete. • ECC playground has been relocated. • The month of July will focus on emergency egress foundations and steel installation. 	<i>Project Milestones</i>
	<ul style="list-style-type: none"> • No new community comments. • Design completion – January 2025 • Start construction – May 2025 • Complete Addition – June 2026

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$4,952,500	\$5,173,546	\$5,049,993
Soft Cost/FFE	\$437,500	\$378,537	\$347,603
Contingency	\$255,000	\$92,917	\$141,692
PROJECT TOTAL	\$5,645,000	\$5,645,000	\$5,539,288

GENERAL INFORMATION

Architect: BVH
 Construction Manager: Prairie Const.
 Project Phase: Under Construction

UNDERWOOD HILLS ELEMENTARY SCHOOL



Summary:

Based upon a facilities task force that was completed in December 2022, the Underwood Hills Elementary School will have upgrades to the mechanical system and a small addition to provide a secure vestibule.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> • Addition project <ul style="list-style-type: none"> ○ Interior demo is complete. ○ Foundations for the addition are complete. ○ Building painting has started. ○ The month of July will focus on steel erection, building painting, and window installation. • Mechanical/Intercom project <ul style="list-style-type: none"> ○ Intercom wiring is in progress. ○ Mechanical valves are on site and install will occur in July. ○ The new mechanical equipment delivery has been delayed and installation will be scheduled around school operations. 	<ul style="list-style-type: none"> • No new community comments.
	<i>Project Milestones</i>
	<ul style="list-style-type: none"> • Design completion – January 2025 • Start construction – May 2025 • Complete renovations – June 2026

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$1,200,000	\$1,200,000	\$1,183,185
Soft Cost/FFE	\$135,000	\$150,652	\$150,652
Contingency	\$60,000	\$44,348	\$44,348
PROJECT TOTAL	\$1,395,000	\$1,395,000	\$1,378,185

GENERAL INFORMATION

Architect: TACK Architects
Construction Manager: *7er/Black Hawk
Project Phase: Under Construction

*7er is the General Contractor for the secure vestibule project. Black Hawk Construction is the General Contractor for the Mechanical upgrades.

SECURITY ENHANCEMENT PROJECT

Summary:

Westside Community School District engaged a Design Advisory Committee (DAC) made up of administration, teachers, and community members to review District facilities regarding physical safety and security and provide design recommendations. Morrissey Engineering was hired in the fall of 2023 to review and update the District's security assessment completed in Bond Phase I. The Assessment made District wide recommendations that were reviewed by the DAC. The security enhancement project will be funded by the interest generated from the bond issuance.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> The panic button wiring is complete. Device install is in progress The month of July will focus on panic button integration. 	<ul style="list-style-type: none"> No new community comments.
	<i>Project Milestones</i>
	<ul style="list-style-type: none"> Install panic buttons – March 2025 to July 2025

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$419,000	\$250,925	\$230,925
Soft Cost/FFE	\$318,500	\$487,689	\$471,787
Contingency	\$12,500	\$11,386	\$11,386
PROJECT TOTAL	\$750,000	\$750,000	\$714,098

GENERAL INFORMATION	
Architect:	N/A
Construction Manager:	N/A
Project Phase:	Under Construction

LOVELAND ELEMENTARY



Summary:

Based upon a facilities task force that was completed in December of 2022, Loveland Elementary will be replaced by a new two-section school located on the same site as the current Loveland Elementary School (8201 Pacific Street, Omaha NE, 68114). The current Loveland Elementary School will be decommissioned and razed prior to the start of the new school. Students will relocate to the swing school during the project.

This new school will be approximately 51,080 sf and incorporate historical attributes and/or materials from the existing elementary school. It will include: a separate cafeteria and gymnasium, dedicated elective classroom space, improved drop off and pick up access, upgraded security and entrance vestibules, improved ADA access, and the construction of FEMA-rated storm shelters. The new elementary school will need to be designed to allow project-based learning areas. It must also provide a safe, healthy, and secure environment for educators, learners, and staff.

<i>Project Updates</i>	<i>Community Comments</i>
<ul style="list-style-type: none"> DAC meetings have continued. Concept Design was approved by the BOE on June 16, 2025. A community meeting was held in June to review the concept design. The month of July will focus on schematic design. 	<i>Project Milestones</i>
	<ul style="list-style-type: none"> Community Engagement was held on June 24, 2025. Desire to have a design that integrates with the neighborhood. Desire to have outdoor community space/park.

	BUDGET	PROJECTED COST	COMMITTED COST
Construction	\$18,717,374	\$18,717,374	\$0
Soft Cost/FFE	\$2,641,738	\$2,641,738	\$1,476,460
Contingency	\$1,920,888	\$1,920,888	\$0
PROJECT TOTAL	\$23,280,000	\$23,280,000	\$1,476,460

GENERAL INFORMATION

Architect: BVH Architecture
 Construction Manager: TBD
 Project Phase: In Design



Westside Community Schools Bond Phase II Project Status



Project	Design					Construction					
	Design Procurement	Concept	Schematic	Design Development	Construction Documents	Contractor Procurement	Bidding	Construction	Sitework	Closeout	11 month Warranty
Hillside Elementary School											
Westgate Elementary School											
Westside Middle School Cafeteria Expansion											
ABC Building Renovations											
Westside High School											
Bathroom Renovations											
Locker Room Renovations											
Cafeteria Expansion											
Foundation Project (NON BOND)											
Westbrook Elementary School Façade and HVAC Replacement											
Paddock Road Elementary School Gym & ECC											
Rockbrook Road Elementary School Gym & ECC											
Underwood Hills Infrastructure upgrades											
Loveland Elementary School											
COMPLETE											
IN PROGRESS											
FUTURE											



Westside Community Schools Master Project Summary Dates

Project	DESIGN PROCESS									CMR PROCESS									BOE		
						Architect Contract	BOE			BOE CMR process	District Issue				CMR Contract		GMP	Architect	CMR		
	Design RFP Issued	Preproposals Meeting	RFP Due	Architect Shortlist	Architect Interviews	BOE Approval	Concept Approval	BOE SD Update	BOE DD Approval	Approval	CMR RFQ	RFQ Due	Short list meeting	CMR Interviews	CMR Selection	Approval	Approval	shortlist / Interview	Shortlist / Interview		
Hillside	05/10/23	05/17/23	06/08/23	06/09/23	06/14/23	07/17/23	10/17/23	12/11/23	03/04/24	11/20/23	12/04/23	01/10/24	01/12/24	01/19/23	01/24/24	02/05/24	07/15/24	MVG / DB	SR/MVG		
Westgate	05/10/23	05/17/23	06/08/23	06/12/23	06/15/23	07/17/23	10/02/23	11/06/23	02/20/24	10/17/23	10/30/23	11/30/23	12/04/23	12/08/23	12/08/23	01/16/24	06/10/24	MVG / DB	AY/AY		
WMS	06/12/23	06/20/23	07/11/23	07/13/23	07/24/23	08/07/23	10/17/23	10/17/23**	01/16/24	11/06/23	11/07/23	12/08/23	12/12/23	12/19/23	12/22/23	01/16/24	05/20/24	KK / MVG	KK / MVG		
ABC	06/12/23	06/20/23	07/11/23	07/13/23	07/27/23	08/07/23	11/06/23	11/6/23**	02/05/24	11/06/23	11/07/23	12/08/23	12/13/23	12/20/23	12/22/23	01/16/24	05/20/24	KK / AY	MVG / KK		
WHS Bathrooms	07/11/23	06/18/23	08/08/23	08/15/23	08/23/23	09/05/23	11/06/23	11/6/23**	01/16/24	HARD BID IN FEBRUARY OF 2024. AWARD MARCH 2024								03/18/24	/ MVG		
WHS Locker room and Café	07/11/23	06/18/23	08/08/23	08/15/23	08/23/23	09/05/23	01/16/24	01/16/24	04/22/24	03/10/25	03/14/25	04/16/25	04/18/25	04/23/25	04/25/25	05/12/25	09/08/25	/ MVG	MVG / MVG		
Westbrook	04/01/24	04/12/24	04/26/24	04/29/24	05/08/24	05/20/24	10/07/24	10/07/24	01/13/25	10/07/24	10/14/24	11/14/24	11/18/24	11/22/24	11/26/24	12/09/24	05/20/25	SR/MVG	AY/AY		
Paddock Road	03/04/24	03/12/24	03/28/24	04/03/24	04/09/24	04/22/24	09/03/24	09/03/24	11/18/24	09/16/24	09/17/24	10/18/24	10/23/24	10/30/24	11/01/24	11/04/24	02/18/25	AY/AY	MVG/MVG		
Rockbrook	03/04/24	03/12/24	03/28/24	04/04/24	04/10/24	04/22/24	09/03/24	09/03/24	12/09/24	09/16/24	09/17/24	10/18/24	10/23/24	10/31/24	11/01/24	11/04/24	03/10/25	SR/DB	BM/SR		
Underwood Hills						08/19/24				HARD BID IN JANUARY OF 2025. AWARD FEBRUARY 2025									02/18/25		
Loveland	01/06/25	01/13/25	02/05/25	02/07/25	02/13/25	02/18/25	06/16/25	08/18/25	01/12/26	08/04/25	08/19/25	09/19/25	09/23/25	09/29/25	10/01/25	10/06/25	04/27/26	AY/AY			
WHS Foundation Addition and Renovation									12/11/23	02/05/24	09/05/23	08/03/23	09/07/23	09/08/23	09/14/23	09/15/23	10/17/23	07/15/24		BM / BM	

APPROVED
SCHEDULED

*All dates are tentative and subject to change based on design progress.
** Concept presentation included schematic design

BOE = Board of Education
SD = Schematic Design
DD = Design Development
CMR = Construction Manager at Risk
RFQ = Request for Qualifications
GMP = Guaranteed Maximum Price





Architect Procurement	Contractor Procurement
Concept Design	Project bidding
Schematic	Construction
Design Development	
Construction Documents	

